[Company name]

DATE: 2026/9/12

PREPARED BY: [Name]

Raw Data

Work component ID	Work component name	Work component type	Work component owner	Milestone	Critical	Planned start date	Actual start date	Planned finish date	Percent complete
3	Widget marketing campaign	Project	Anna Franklin	No	Yes	2006/1/1	2006/1/2	2006/3/1	100.00%
3.1	Campaign message developed	Sub-project	Anna Franklin	Yes	No	2006/1/1	2006/1/10	2006/3/1	100.00%
3.1.1	Establish PR lists	Activity	Frank Taylor	No	Yes	2006/1/1	2006/1/2	2006/3/1	100.00%
3.2	Create campaign execution plan	Sub-project	Anna Franklin	Yes	No	2006/2/1	2006/2/1	2006/2/5	100.00%

Estimated finish date	Actual finish date	Planned budget	Actual cost to date	Cost estimate at completion	Planned resource hours	Actual resource hours to date	Resource hours estimate at completion
2006/3/1	2006/3/15	$5,100.00	$5,600.00	$5,600.00	9000	9500	92
2006/3/1	2006/3/15	$3,000.00	$3,100.00	$3,100.00	4000	4200	42
2006/3/1	2006/3/2	$2,000.00	$2,500.00	$2,500.00	4000	4300	40
2006/2/5	2006/2/5	$100.00	$0.00	$0.00	1000	950	10

Schedule notes	Schedule recovery plan	Cost notes	Cost recovery plan	Resource notes	Resource recovery plan	Note from work component owner

[Company name]

DATE: 2026/9/12

PREPARED BY: [Name]

Project Status Report

PROJECT SUMMARY

Project name: Widget marketing campaign

Project Manager: Anna Franklin

Reporting period

From: 2006/1/1

To: 2006/6/1

Report date: 2026/9/12

Project Total

WORK COMPONENT DETAILS

Work Component ID	Work Component Name	Work Component Type
3.1	Campaign message developed	Sub-project
3.1.1	Establish PR lists	Activity
3.2	Create campaign execution plan	Sub-project

Planned Start Date	Actual Start Date
2006/1/1	2006/1/2

Work Component Owner	Milestone	Critical	Planned StartDate	Actual Start Date
Anna Franklin	Yes	No	2006/1/1	2006/1/10
Frank Taylor	No	Yes	2006/1/1	2006/1/2
Anna Franklin	Yes	No	2006/2/1	2006/2/1

Schedule				
Planned Finish Date	Est./ Actual Finish Date	Complete?	Variance %	Schedule Status
2006/3/1	2006/3/15	1	-24%	3

Planned Finish Date	Est. / Actual Finish Date	Complete?	Schedule Variance %	Schedule Status	Schedule Notes
2006/3/1	2006/3/15	1	-23.7%	3	
2006/3/1	2006/3/2	1	-1.7%	1	
2006/2/5	2006/2/5	1	0.0%	1	


	Budget				
	Planned Budget	Actual Cost to Date	Variance	Variance %	Budget Status
	$5,100	$5,600	-$500	-9.8%	1

Schedule Recovery Plan	Planned Budget	Actual Cost to Date	Budget Variance	Budget Variance %	Budget Status	Cost Notes
	$3,000	$3,100	-$100	-3.3%	1	
	$2,000	$2,500	-$500	-25.0%	2	
	$100	$0	$100	100.0%	1	

	Resources				
	Planned Hours	Actual Hours to Date	Variance	Variance %	Resources Status
	9000.0	9500.0	-450.0	-5.0%	3


Cost Recovery Plan	Planned Resource (Hrs)	Actual Hours to Date	Resource Variance (Hrs)	Resource Variance %	Resource Status
	4000.0	4200.0	-200.0	-5.0%	3
	4000.0	4300.0	-300.0	-7.5%	3
	1000.0	950.0	50.0	5.0%	1

Resource Notes	Resource Recovery Plan

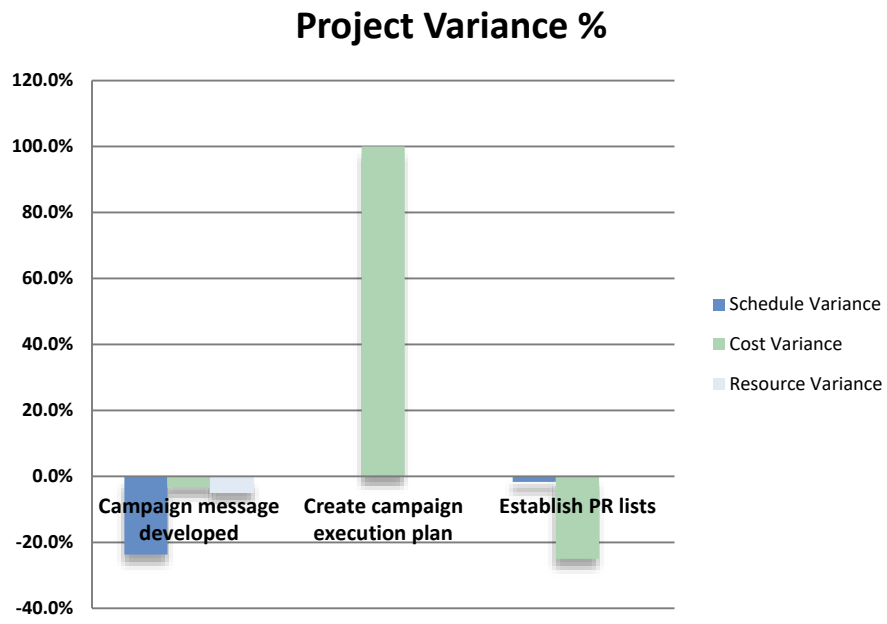

Milestone	(All)
Critical	(All)

Values		
Schedule Variance	**Cost Variance**	**Resource Variance**
-0.254237288	0.716666667	-0.075

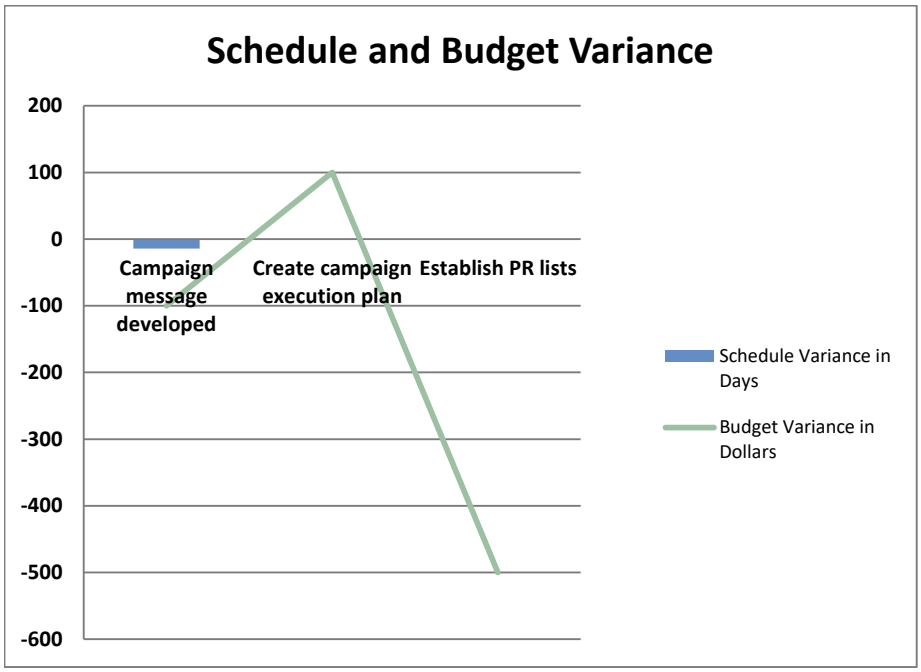

Milestone	(All)
Critical	(All)

Budget Variance in Dollars
-500

Milestone	(All)
Critical	(All)

[Company name]

DATE: 2026/9/12

PREPARED BY: [Name]

Assumptions and Notes

Variance threshold definition

VARIANCE	VARIANCE TYPE	THRESHOLD AMOUNT	THRESHOLD %
Schedule	Days	20	20.0%
Budget	Dollars	$1,200	20.0%
Resource hours	Hours	20	20.0%

Note to report audience:
